

**ADDENDUM
NO. 01**

January 20, 2026

Kalamazoo Public Schools Chenery Auditorium Lighting Replacement
714 South Westnedge Avenue
Kalamazoo, MI 4900

TO: ALL BIDDERS OF RECORD

This Addendum forms a part of and modifies the Bidding Requirements, Contract Forms, Contract Conditions, the Specifications and the Drawings dated January 8, 2026, by TowerPinkster. Acknowledge receipt of the Addendum in the space provided on the Bid Form. Failure to do so may subject the Bidder to disqualification.

This Addendum consists of Pages ADD 1-1 through ADD 1- 1.







A. SPECIFICATION SECTION 01 32 00 – SCHEDULES AND REPORTS


a. 1.03 GUIDELINE SCHEDULE

Add:

1. See Guideline Schedule attached.
2. See Site logistics attached.

Activity Name	Original Duration	Start	Finish	2026																								2027																					
				December				January			February			March			April			May			June			July			August			September			October			November			December			January					
				0	0	1	2	2	0	1	1	2	2	0	0	1	2	0	0	1	2	3	0	1	2	2	0	1	2	2	0	1	1	2	3	0	1	2	2	0	0	1	2	3	0	1	2	2	0
KPS CEC & Chenery Auditorium Lighting Replace	181	08-Jan-26	18-Sep-26	<div><div></div></div> 18-Sep-26, KPS CEC & Chenery Auditorium Lighting Replace																																													
Administration	181	08-Jan-26	18-Sep-26	<div><div></div></div> 18-Sep-26, Administration																																													
Bidding and Contracts	46	08-Jan-26	12-Mar-26	<div><div></div></div> 12-Mar-26, Bidding and Contracts																																													
Owner Advertisement and Posted to Planroom	0	08-Jan-26*		<div><div></div></div> Owner Advertisement and Posted to Planroom																																													
Addendum 01	1	20-Jan-26	20-Jan-26	<div><div></div></div> Addendum 01																																													
Pre-Bid Meeting	1	22-Jan-26*	22-Jan-26	<div><div></div></div> Pre-Bid Meeting																																													
Bids Due	0		03-Feb-26	<div><div></div></div> Bids Due																																													
Review and Post Bid Tabs	2	04-Feb-26	05-Feb-26	<div><div></div></div> Review and Post Bid Tabs																																													
Pre-Award Conferences	3	05-Feb-26*	09-Feb-26	<div><div></div></div> Pre-Award Conferences																																													
Letter Of Recommendation	0		09-Feb-26	<div><div></div></div> Letter Of Recommendation																																													
KPS Board Approval	0	19-Feb-26*		<div><div></div></div> KPS Board Approval																																													
Notice To Proceed	0	20-Feb-26*		<div><div></div></div> Notice To Proceed																																													
Contract Execution	15	20-Feb-26*	12-Mar-26	<div><div></div></div> Contract Execution																																													
Pre-Construction	110	23-Feb-26	24-Jul-26	<div><div></div></div> 24-Jul-26, Pre-Construction																																													
Submittals and Shop Drawings	30	23-Feb-26*	03-Apr-26	<div><div></div></div> Submittals and Shop Drawings																																													
Material Procurement	110	23-Feb-26*	24-Jul-26	<div><div></div></div> Material Procurement																																													
Pre-Construction Meeting	0	03-Mar-26*		<div><div></div></div> Pre-Construction Meeting																																													
Procure Permits	10	20-Apr-26*	01-May-26	<div><div></div></div> Procure Permits																																													
Pre-Demolition Conference	0	21-May-26*		<div><div></div></div> Pre-Demolition Conference																																													
KPS Last Day of School	1	05-Jun-26*	05-Jun-26	<div><div></div></div> KPS Last Day of School																																													
Mobilize (Dumpsters, Floor Protection, Dust Protection, Etc.)	0	08-Jun-26*		<div><div></div></div> Mobilize (Dumpsters, Floor Protection, Dust Protection, Etc.)																																													
Pre-Installation Conferences	5	15-Jun-26*	19-Jun-26	<div><div></div></div> Pre-Installation Conferences																																													
Closeout	26	13-Aug-26	18-Sep-26	<div><div></div></div> 18-Sep-26, Closeout																																													
Contractor Closeout Meeting	0	13-Aug-26*		<div><div></div></div> Contractor Closeout Meeting																																													
Final Cleaning of Surrounding Auditorium Areas	5	17-Aug-26*	21-Aug-26	<div><div></div></div> Final Cleaning of Surrounding Auditorium Areas																																													
KPS, TP, and TSC Punchlist Creation	2	18-Aug-26	19-Aug-26	<div><div></div></div> KPS, TP, and TSC Punchlist Creation																																													

 Actual Work  Remaining Work  Critical Remaining Work  Milestone  Summary	224050.19 - KPS CEC & Chenery Auditorium Lighting Replacement Guideline Schedule - 19-Jan-26 Page 1 of 2	
---	--	---

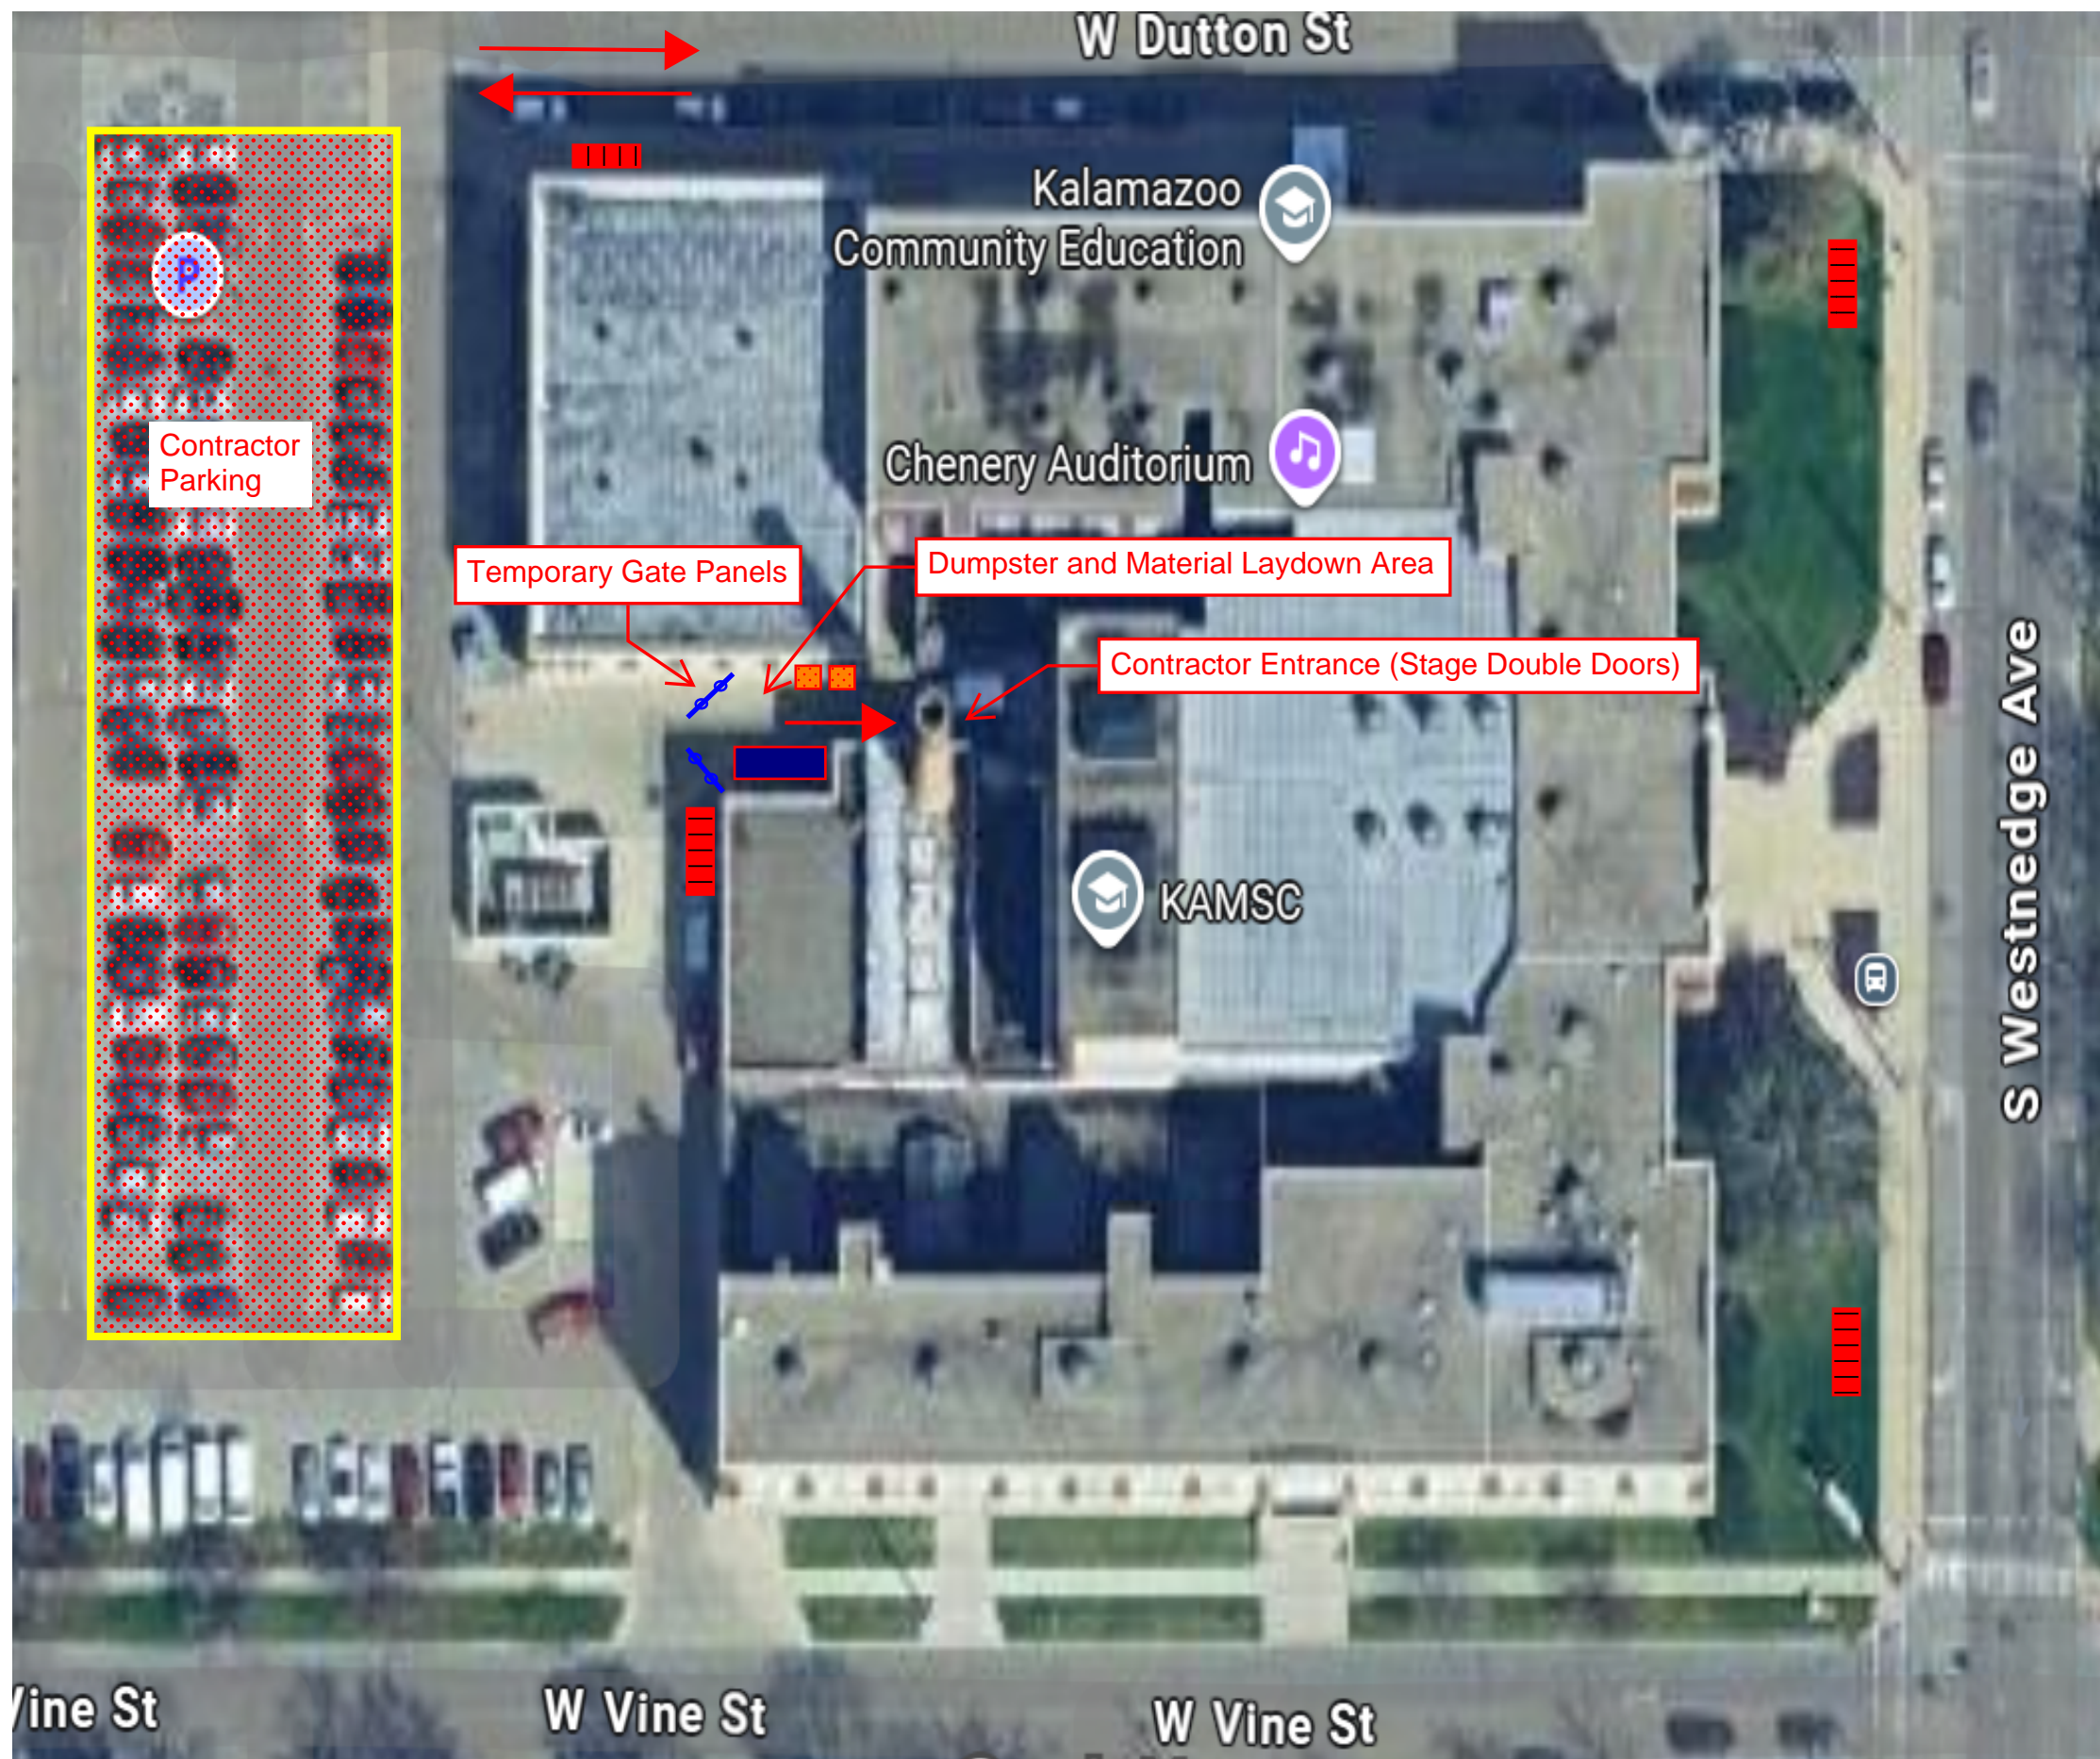

Kalamazoo Public Schools CEC & Chenery Auditorium Lighting Replacement Project

Kalamazoo Public Schools


Every child. Every opportunity. Every time.

Legend:

Contractor Parking



Fence Panels



Dumpsters



Temp. Toilets



Project Signage



TowerPinkster

Architecture · Engineering · Interiors



The SKILLMAN Corporation

AN EMPLOYEE-OWNED COMPANY

SITE LOGISTICS PLAN

12/29/2025
